CIVIL QUALITY CONSULTANTS & ENGINEERS

(Buildings Geo-Tech & Highway Materials Testing Laboratory)
An ISO 9001: 2015 Certified Company
NABL Accredited As Per ISO/IEC : 17025:2005 Laboratory

JAS-ANZ
ISO 9001:2000 CERTIFIED

No: CQCE/3rd Party/RRN Division/39/ 2018-19 Date: 04.01.2019

To,
Executive Engineer,
Electrical – RRN Zone Division
BBMP, Bangalore.

Sir

Sub:- Submission of 3rd Party Report for the work of Providing Street Lights in Ward No.16, BBMP, Bangalore.

Ref:-

Ref:- :- (i) **Work order No.** EE(Elec)/RRN/WO/49/2018-19 Dated: 29.10.2018
(ii) **Job code No.** 038-18-000004

Adverting to the above, we would like to submit the 3rd Party Inspection Report for the above said work in Electrical – RRN Zone Division along with Mr. Ramesh (Assistant Executive Engineer, Electrical South Zone), and Mr. Kumar (Electrtical Engineer, 3rd Party Consultants), Bangalore on 05.01.2019

The following works inspected the details of works inspected is as follows,

Sl no	Name of the work	Amount of estimate Rs in Lakhs.	Remarks
1	Providing Street Lights in Ward No.16, BBMP, Bangalore.	Rs. 10.00 Lakhs (1st and Final bill)	Work carried out satisfactorily Details mentioned in 3rd party compliance report

The details of works and measurements checked during the inspection time in the presence if the officials /officers afore said.

This is for favor of kind information and needful in the matter.

Enclosures: 3rd part Inspection report
Thanking you

EE (Ele.)

CIVIL QUALITY CONSULTANTS & ENGINEERS Bangalore

yours faithfully

Authorized signatory

CIVIL QUALITY CONSULTANTS & ENGINEERS

(Buildings Geo-Tech & Highway Materials Testing Laboratory)
An ISO 9001: 2015 Certified Company
NABL Accredited As Per ISO/IEC : 17025:2005 Laboratory

JAS-ANZ
ISO 9001:2000 CERTIFIED

Name of Work : **Providing Street Lights in Ward No.16, BBMP, Bangalore.**

Contractor/Agency	:	**Executive Engineer-3**, KRIDL, Bangalore.
Name of Client	:	**Executive Engineer,** Electrical-RRN Division, BBMP, Bangalore.
Total Bill Cost in Lakhs	:	Rs.9.90 Lakhs
Date Of Inspection	:	04.01.2019
Items of Bill	:	First & Final Bill
In the Presence of	:	(a) **Mr. Ramesh (Assitant Executive Engineer, Electrical RRN Zone),** BBMP, Bangalore.
	:	(b) **Mr. kumar,** (Electrical Engineer) M/s Civil Quality Consultants & Engineers, Bangalore.

3rd Party Compliance Report

Sl. No.	Description of the Item	Unit	Quantity	Comments / observations
1	Supply of solar lux level street light controller single phase 3KV	Each	2	Supplied Material Quality found satisfactory
2	Wiring for lighting/power circuit using one of FRLS PVC insulated 1100 V Grade,multistrand copper with	P/Mtr	4	Supplied Material Quality found satisfactory
	6 Sqmm	P/Mtr	8	Supplied Material Quality found satisfactory
3	LED Street light, Supply of 90Watts LED Street light with Pressure die cast aluminum housing body with optimal heat sink for netter thermal	Each	25	Supplied Material Quality found satisfactory
4	Supplying and fixing....mm dia class A GI pipe bracket up to 2.7 meters long terminated with a reducing collar of 40x25mm	Each	25	Supplied Material Quality found satisfactory

CIVIL QUALITY CONSULTANTS & ENGINEERS Bangalore

Providing Street Lights in Ward No.16, BBMP, Bangalore.

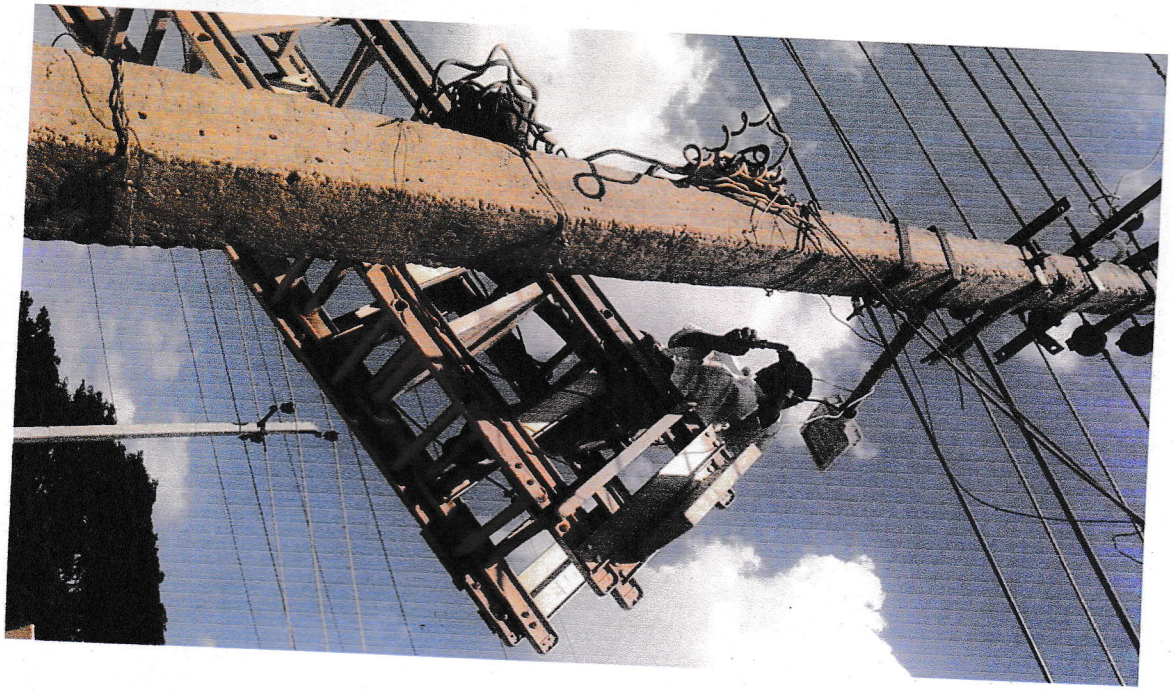

QUALITY CONSULTANTS & ENGINEERS
Bangalore
